

City of Bend Transportation GO Bond Program

Monthly Progress Report

August 2013



HDR

In association with the Bend offices of the following firms:



DevTech Engineering, LLC
Site Planning · Civil Engineering


For the latest project information, visit www.bendoregon.gov/gobond

or to leave comments/questions call 541-388-5547 or email streetbond@ci.bend.or.us

City of Bend Transportation GO Bond Program: Monthly Project Report Number 20: August 2013

PROGRAM SUMMARY

COST: **City of Bend Transportation GO Bond Program Expenditure Status**

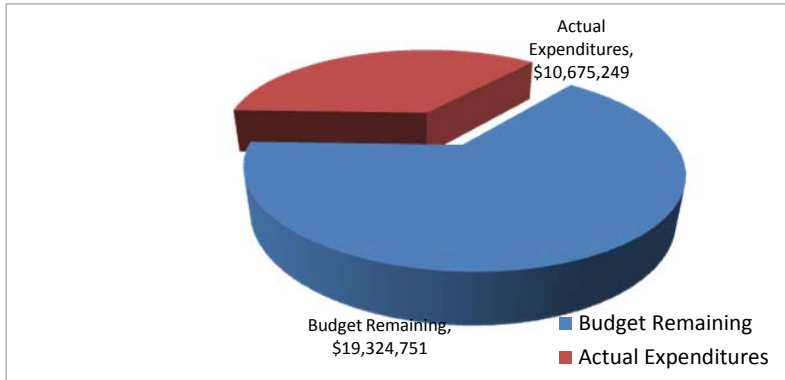

SCHEDULE:

	2012				2013				2014				2015			
	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4
Simpson / Mt. Wash. Intersection	█	█	█	█	Complete											
18th / Empire Intersection	█	█	█	█	Complete											
Powers / Brookwood Intersection	█	█	█	█	Complete											
Reed Mkt: Newberry - 27th St	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
Reed Mkt: Newberry - 3rd Street	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█	█
27th St. Reconstruction	To Be Determined - part of SE Sewer Interceptor project															

Individual Project Status						
MPR Page #	Project #	Proj Name	Overall Status	Project Delivery Step	Design Complete %	Construction Complete %
2	1a	Empire / 18th Intersection	G	Completed	100%	100%
3	1b	Simpson / Mt Washington Intersection	G	Completed	100%	100%
4	1c	Powers / Brookwood Intersection	G	Completed	100%	100%
5	2a	Reed Market: Newberry - 27th	G	Construction	100%	20%
6	2d	Reed Market: Newberry - 3rd	Y	Preliminary Eng.	95%	0%

	Definitions for Schedule and Budget Status
Green	Schedule: Project is no more than 5 days behind schedule. Budget: Project is within budget.
Yellow	Schedule: Project is between 6 and 30 days behind schedule. Budget: Project is between 1% and 10% over budget.
Red	Schedule: Project is over 30 days behind schedule. Budget: Project is more than 10% over budget.



Project 1a - EMPIRE / 18TH INTERSECTION

City Project #: ST12CB

Project Phase: Construction

OVERALL	G
SCHEDULE	G
BUDGET	G

City of Bend Project Manager: Nick Arnis
Program Mgmt Consultant: HDR Engineering
Program Manager: Stephanie Serpico
Design Consultant: HDR Engineering
Project Manager: Brad Shea
Contractor: Knife River

Percent Complete:

Design: 100%

Construction: 100%



Project Scope Summary

Upgrade the existing stop controlled intersection to improve safety and reduce congestion. Construct a roundabout, sidewalks, landscaping strips, storm water facilities, illumination, signs and striping to current city standards.

Project Activities / Accomplishments

None.

Schedule Milestone Summary

Design	Approved	Forecast	Actual
Concept	Feb-12	Feb-12	2/10/2012
30% Submittal	Feb-12	Feb-12	2/29/2012
60% Submittal	Mar-12	Mar-12	3/27/2012
95% Submittal	Apr-12	Apr-12	4/23/2012
Final Submittal	May-12	May-12	5/7/2012
Advertisement Date	May-12	May-12	5/22/2012
Construction Step	Approved	Forecast	Actual
Bid Date	Jun-12	Jun-12	6/12/2012
Contractor NTP	Jun-12	Jun-12	7/6/2012
Construction Complete	Oct-12	Nov-12	11/19/2012

Upcoming Project Activities

None.

Financial Milestone Summary

Baseline Project Budget - GO Bond only		\$3,188,812	
Current Budget - GO Bond only		\$2,909,010	
Non GO Bond Budget		\$0	
Total Project Budget		\$2,909,010	
Cost Item	Budget	Forecast	Expended
Total	\$2,909,010	\$2,669,526	\$2,546,277

Issues Being Worked

Striping - temporary striping is being placed in lieu of durable stripes because of temperatures. Permanent striping will be placed in June 2013.



Project 1b - SIMPSON / MT WASHINGTON INTERSECTION

City Project #: ST12CC

OVERALL	G
SCHEDULE	G
BUDGET	G

Project Phase: Construction

City of Bend Project Manager: Nick Arnis
Program Mgmt Consultant: HDR Engineering
Program Manager: Stephanie Serpico
Design Consultant: WH Pacific
Project Manager: Barry Johnson
Contractor: Jack Robinson & Sons

Percent Complete: :
Design: 100%
Construction: 100%



Project Scope Summary
 Upgrade the existing stop controlled intersection to improve safety and reduce congestion. Construct a roundabout, sidewalks, landscaping strips, storm water facilities, illumination, signs and striping to current city standards.

Project Activities / Accomplishments
 None

Schedule Milestone Summary			
Design	Approved	Forecast	Actual
Concept	Jan-12	Jan-12	1/17/2012
30% Submittal	Jan-12	Jan-12	1/26/2012
60% Submittal	Feb-12	Feb-12	2/24/2012
95% Submittal	Apr-12	Apr-12	4/4/2012
Final Submittal	Apr-12	Apr-12	4/23/2012
Advertisement Date	May-12	May-12	5/7/2012
Construction Step	Approved	Forecast	Actual
Bid Date	May-12	May-12	5/29/2012
Contractor NTP	Jun-12	Jun-12	6/20/2012
Construction Complete	Sep-12	Oct-12	10/26/2012

Upcoming Project Activities
 None

Financial Milestone Summary			
Baseline Project Budget - GO Bond only		\$2,742,916	
Current Project Budget - GO Bond only		\$2,518,129	
Non GO Bond Budget		\$514,000	
Total Project Budget		\$3,032,129	
Cost Item	Budget	Forecast	Expended
Total	\$3,032,129	\$2,483,513	\$2,255,819

Issues Being Worked
 Striping - temporary striping is being placed in lieu of durable stripes because of temperatures. Permanent striping will be placed in June 2013.

Project 1c - POWERS / BROOKSWOOD INTERSECTION

City Project #: ST12CD

Project Phase: Construction

OVERALL	G
SCHEDULE	G
BUDGET	G

City of Bend Project Manager: Nick Arnis
 Program Mgmt Consultant: HDR Engineering
 Program Manager: Stephanie Serpico
 Design Consultant: DEA
 Project Manager: Kevin Bracy
 Contractor: Jack Robinson & Sons

Percent Complete:

Design: 100%

Construction: 100%

Project Scope Summary

Upgrade the existing stop controlled intersection to improve safety and reduce congestion. Construct a roundabout, sidewalks, landscaping strips, storm water facilities, illumination, signs and striping to current city standards.

Project Activities / Accomplishments

None.



Schedule Milestone Summary

Design	Approved	Forecast	Actual
Concept	Feb-12	Feb-12	2/10/2012
30% Submittal	Feb-12	Feb-12	2/21/2012
60% Submittal	Mar-12	Mar-12	3/27/2012
95% Submittal	Apr-12	Apr-12	4/23/2012
Final Submittal	May-12	May-12	5/7/2012
Advertisement Date	May-12	May-12	5/22/2012
Construction Step	Approved	Forecast	Actual
Bid Date	Jun-12	Jun-12	6/13/2012
Contractor NTP	Jul-12	Jul-12	6/20/2012
Construction Complete	Oct-12	Nov-12	11/16/2012

Upcoming Project Activities

None.

Financial Milestone Summary

Baseline Project Budget - GO Bond only	\$2,656,385		
Current Project Budget - GO Bond only	\$2,515,346		
Non GO Bond Budget	\$0		
Total Project Budget	\$2,515,346		
Cost Item	Budget	Forecast	Expended
Total	\$2,515,346	\$2,207,272	\$2,062,087

Issues Being Worked

Striping - temporary striping is being placed in lieu of durable stripes because of temperatures. Permanent striping will be placed June 2013.



Project 2a - REED MARKET: NEWBERRY - 27th

City Project #: ST12CE

Project Phase: Construction

OVERALL	G
SCHEDULE	G
BUDGET	G

City of Bend Project Manager: Nick Arnis
 Program Mgmt Consultant: HDR Engineering
 Program Manager: Stephanie Serpico
 Design Consultant: Devtech
 Project Manager: Chris Chambers
 Contractor: Jack Robinson & Sons

Percent Complete:

Design: 100%
 Construction: 20%

Project Scope Summary

Upgrade the existing roadway to current City of Bend standards to a major arterial. This includes a two travel lanes and a continuous center turn lane, 6 foot shoulders/bike lanes, separated 6 foot sidewalks and landscape strip. Construct new storm water facilities, signing, illumination, retaining walls and striping.

Project Activities / Accomplishments

Finished grading the roadway, installing storm water system and drywells, and retaining walls. Poured sidewalks, curb and medians. Installed landscape swales.



Schedule Milestone Summary

Design	Approved	Forecast	Actual
Concept	May-12	May-12	4/26/2012
30% Submittal	May-12	May-12	6/11/2012
60% Submittal	Aug-12	Oct-12	10/18/2012
95% Submittal	Nov-12	Jan-13	1/25/2013
Final Submittal	Mar-13	Feb-13	2/6/2013
Advertisement Date	Mar-13	Mar-13	3/18/2013
Construction Step	Approved	Forecast	Actual
Bid Date	Apr-13	Apr-13	4/16/2013
Contractor NTP	May-13	May-13	5/13/2013
Construction Complete	Nov-13	May-14	

Upcoming Project Activities

Begin paving the bike lanes and travel lanes.

Financial Milestone Summary

Baseline Project Budget - GO Bond only	\$6,073,962		
Current Project Budget - GO Bond only	\$6,134,544		
Non GO Bond Budget	\$0		
Total Project Budget	\$6,134,544		
Cost Item	Budget	Forecast	Expended
Total	\$6,134,544	\$5,027,003	\$1,863,493

Issues Being Worked

None at this time.



Project 2d - REED MARKET: NEWBERRY TO 3rd STREET

City Project #'s: ST12CJ

Project Phase: Preliminary Eng. Class 3

OVERALL	G
SCHEDULE	Y
BUDGET	G

City of Bend Project Manager: Nick Arnis
 Program Mgmt Consultant: HDR Engineering
 Program Manager: Stephanie Serpico
 Design Consultant: HWA / CW
 Project Manager: Mark Douglas / Jim Lord
 Contractor: TBD

Percent Complete:
 Design: 95%
 Construction: 0%



Project Scope Summary
 Upgrade the existing roadway to current City of Bend standards to a major arterial. This includes a two travel lanes and a continuous center turn lane, 6 foot shoulders/bike lanes, separated 6 foot sidewalks and landscape strip. Construct new storm water facilities, signing, lighting, retaining walls and striping. Upgrade the existing the railroad crossing. Realign American Lane to the west of the current location and reconstruct a bridge at the new location. At the intersection of Reed Market and 15th Street, upgrade the existing signalized intersection to improve safety and reduce congestion.



Prior Project Activities / Accomplishments
 Continue working with utility companies on conflicts and relocation plans. Submitted 95% construction plans, specifications and estimate for the City for to review. Held design review meeting to discuss design issues and comments. Continued negotiations for impacted properties between 3rd Street and Newberry Drive. Developed staging options for the intersection of Reed Market and 15th Street and Reed Market west of 9th Street. Will review options with City for concurrence on design.

Schedule Milestone Summary			
Design	Approved	Forecast	Actual
Concept	Jun-12	Jun-12	Jul-12
30% Submittal	Jul-12	Nov-12	11/28/2012
60% Submittal	Oct-12	Mar-13	4/9/2013
95% Submittal	Feb-13	Jul-13	7/8/2013
Final Submittal	Feb-13	Sep-13	
Advertisement Date	Aug-13	Oct-13	
Construction Step	Approved	Forecast	Actual
Bid Date	Sep-13	Oct-13	
Contractor NTP	Oct-13	Nov-13	
Construction Complete	Nov-14	Sep-15	

Upcoming Project Activities
 Continue right of way negotiations. Present approved construction staging options to public.

Financial Milestone Summary : Reed Market: Newberry - 3rd Street			
Baseline Project Budget - GO Bond only		\$13,912,422	
Current Project Budget - GO Bond only		\$14,497,470	
Non GO Bond Budget		\$0	
Total Project Budget		\$14,497,470	
Cost Item	Budget	Forecast	Expended
Total	\$14,497,470	\$13,597,470	\$2,021,450

Issues Being Worked
 Project bidding schedule. There are a few right of way negotiations that are holding up the current project schedule. A new let date needs to be established based on these properties. Construction staging, utility relocations at the intersection of Reed Market and 15th Street, coordinating the railroad crossing construction with BNSF.

